


Activity ID	Activity Name	Duration	Start	Finish	2024					
					Apr	May	Jun	Jul	Aug	
					76	77	78	79	80	
NE2017/03 - ARQ PHASE 2A - Monthly Programme Update (202404)-0_240429		1810	21-Jun-2021 A	30-Oct-2026						
Road Improvement Works Location 1 (RIW1)		527	21-Jun-2021 A	05-Nov-2024						
Construction Works		527	21-Jun-2021 A	05-Nov-2024						
CON12110	Drainage, utilities works & backfilling (RWC2 type 4, 6, 7, 8)	60	21-Jun-2021 A	09-Aug-2024						
CON12130	Road works (RWC2 type 4, 6, 7, 8)	60	26-Jul-2021 A	13-Sep-2024						
CON12134	Install stone facing for wall (RWC2 type 4, 6, 7, 8)	72	02-Aug-2021 A	05-Nov-2024						
CON10770	Install sheet pile & ELS to RW pile cap (RWC2 type 3, stage 2), 1 team	72	02-Jan-2024 A	27-Apr-2024						
CON11328D	Subletting works - socketed H-pile at CT5	36	15-Jan-2024 A	27-Apr-2024						
CON115743	Construct NB RC footing (FE1-F6b to FE1-F7b, 30m, 1.0m/d, 1 team)	18	20-Feb-2024 A	27-Apr-2024						
CON12488	Install lift (KS27 west side)	42	21-Feb-2024 A	29-Apr-2024						
CON12554	Install lift (KS27 east side)	36	21-Feb-2024 A	22-Apr-2024						
CON125561	Backfilling works & hard-landscaping works (KS27 east side)	36	22-Feb-2024 A	27-Apr-2024						
CON10616	ELS works (RWC2 bay6 to bay14)	36	22-Feb-2024 A	27-Apr-2024						
CON10430	Construct RW wall (RWC2 type 5 [bay 46])	36	29-Feb-2024 A	02-May-2024						
CON124891	Backfilling works & hard-landscaping works (KS27 west side)	36	07-Mar-2024 A	06-May-2024						
CON11530	Construct piling foundation on CT6 Type 1 (18nos, 2d/no, 1 team) + 2d for 1st	38	21-Mar-2024 A	09-May-2024						
CON10512	Construct RW footing (RWC2 type 3a Bay 37 to Bay 31)	84	02-Apr-2024 A	30-Jul-2024						
CON11330	Construct CT5 piling foundation (15nos, 6d/no, 1 team + setup)	90	29-Apr-2024	15-Aug-2024						
CON12210	Drainage, utilities works & backfilling (RWC2 type 5)	36	03-May-2024	15-Jun-2024						
CON12570	T&C to lift, submit LE5 and EMSD inspection (KS27 east side)	6	04-May-2024	10-May-2024						
CON10790	Construct RW pile cap / footing (RWC2 type 3, stage 2), 1 team	42	04-May-2024	24-Jun-2024						
CON10652	Construct RW footing (RWC2 bay6 to bay14)	36	04-May-2024	17-Jun-2024						
CON115763	Construct NB RC wall (FE1-F6b to FE1-F7b, 30m, 0.85m/d, 1 team)	24	04-May-2024	01-Jun-2024						
CON12492	T&C to lift, submit LE5 and EMSD inspection (KS27 west side)	1	07-May-2024	07-May-2024						
CON10412	Construct RW footing (RWC2 type 6 [bay 48 to bay 47])	24	08-May-2024	05-Jun-2024						
CON12590	T&C and Statutory Inspection _KS27	30	11-May-2024	17-Jun-2024						
CON11532	Construct piling foundation on CT6 Type 2 (21nos, 2d/no, 1 team)	42	16-May-2024	05-Jul-2024						
CON10514	Construct RW footing (RWC2 type 3a Bay 37 to Bay 31)	84	25-May-2024	02-Sep-2024						
CON11710	Drainage, utilities works, backfilling & road paving (FE1-F4b to FE1-F7b & FE1-	30	03-Jun-2024	09-Jul-2024						
CON10414	Construct RW wall (RWC2 type 6 [bay 48 to bay 47])	24	06-Jun-2024	05-Jul-2024						
CON12230	Road works (RWC2 type 5)	36	17-Jun-2024	29-Jul-2024						
CON10654	Construct RW wall (RWC2 type 2)	48	18-Jun-2024	13-Aug-2024						
CON10810	Construct RW wall (RWC2 type 3, stage 2), 1 team	60	25-Jun-2024	03-Sep-2024						
Road Improvement Works Location 2 (RIW2)		436	26-Nov-2023 A	05-Mar-2025						
Construction Works in Slope C3 (Portion B)		358	26-Nov-2023 A	17-Dec-2024						
CON20250	Fabrication of NB steel post - central median along new clean water bay road 1	182	26-Nov-2023 A	25-May-2024						
CON20330	Fabrication of NB Acoustic panels - central median near junction at on sau roa	105	15-Feb-2024 A	25-May-2024						
CON21116B	(NCE255) Road works at new U-turn bay (Remaining part)	30	28-Feb-2024 A	04-May-2024						
CON21150	Construct hard landscape works at Portion B (Part 1)	60	10-May-2024	22-Jul-2024						
CON21170	Construct hard landscape works at Portion B (Part 2)	60	10-May-2024	22-Jul-2024						
CON21190	Construct hard landscape works at Portion B (Part 3)	60	10-May-2024	22-Jul-2024						
CON20270	Steel post along new clean water bay road to kowloon delivery	24	26-May-2024	18-Jun-2024						
CON20350	Acoustic panels near on sau road left turn to kowloon side delivery	24	26-May-2024	18-Jun-2024						
CON20370	Fabrication of NB Acoustic panels - central median along new clean water bay	182	19-Jun-2024	17-Dec-2024						
Construction Noise Semi-Enclosure SE2 (Portion C)		298	08-Mar-2024 A	05-Mar-2025						
CON22070	Construct NB RC L-shaped wall (SE2 Bay13 to Bay21; L=85m)	54	08-Mar-2024 A	16-May-2024						
CON22590	Road lighting, irrigation system & utilities works	240	17-May-2024	05-Mar-2025						
CON21750	Backfilling, construct road drainage & road paving (CT4, SE2 Bay4 to Bay12; l	60	17-May-2024	27-Jul-2024						
CON22090	Backfilling, construct road drainage & road paving (SE2 Bay13 to Bay21; L=85	54	17-May-2024	20-Jul-2024						
CON22570	Slope improvement Works (pit-by-pit method) (CT4 & SE2 fount part, 250nos p	120	17-May-2024	08-Oct-2024						
CON22610	Application for power supply & energization (RIW2)	156	17-May-2024	20-Nov-2024						
Road Improvement Works Location 3 (RIW3)		1467	19-Jul-2021 A	30-Oct-2026						
Construction Works		1467	19-Jul-2021 A	30-Oct-2026						
CON31130	(NCE215) (CE595) Cut slope works (CH115 to CH200) (L=85m, 13007m3, 11	1300	19-Jul-2021 A	15-Oct-2025						
CON31212	Rock slope mapping (Stage 2)	180	03-Oct-2022 A	21-May-2024						
CON31170	Soil nail works & further construct RWD3 (11NE-D/F246, stage 2)	150	21-Oct-2022 A	09-May-2024						
CON31710	Construct footing, pier & pier head F1-4	144	20-Dec-2022 A	28-May-2024						
CON31214	PM review & acceptance and slope stabilization measures (Stage 2)	180	20-Jan-2023 A	26-Sep-2024						
CON32810	Road works (RWD2 remaining)	42	05-Jun-2023 A	06-May-2024						
CON31290	Reinstatment works & fill no-fine concrete works	90	09-Jun-2023 A	14-Jun-2024						
CON30673	TTA application at SMPR for fresh watermain connection A & B	60	26-Aug-2023 A	27-Apr-2024						
Actual Work Remaining Work Milestone		NE/2017/03 Development of Anderson Road Quarry Site - Investigation Design & Construction Development of Anderson Road Quarry Site Road - Improvement Works & Pedestrian Connectivity Facilities Works Phase 2A 3-Month Rolling Programme							Page 1 of 3	

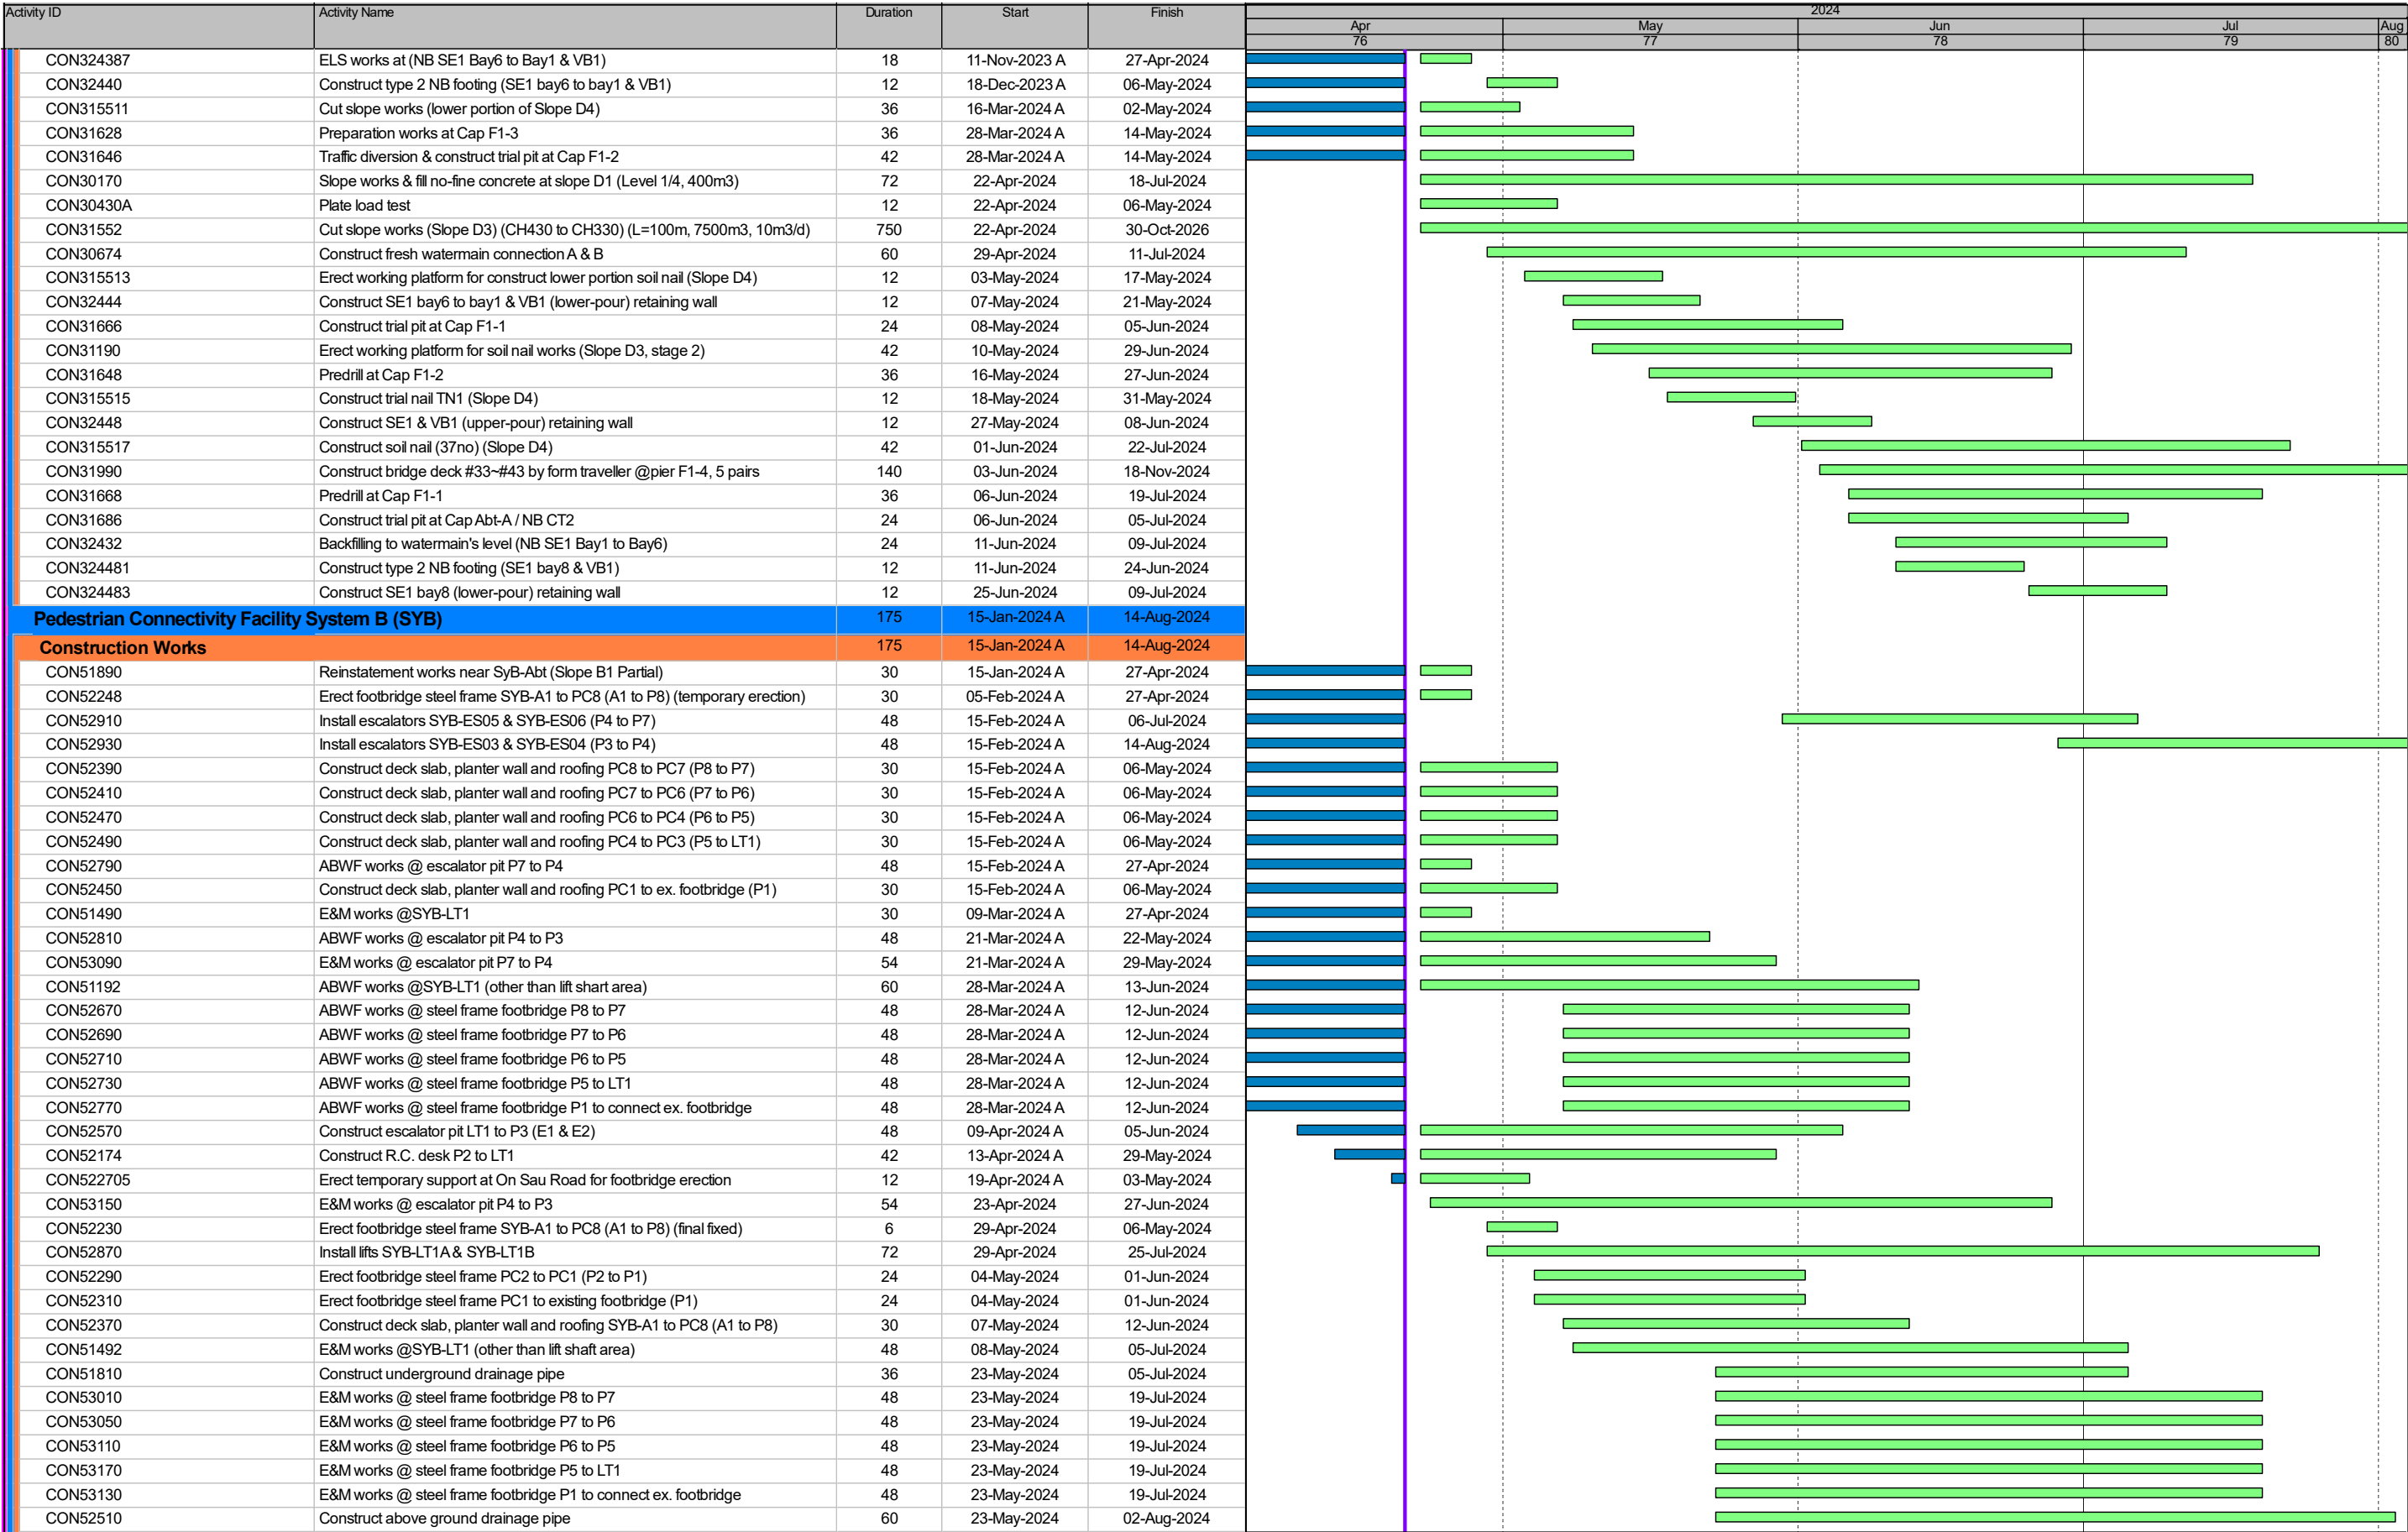

 Actual Work

 Remaining Work

 Milestone

Activity ID	Activity Name	Duration	Start	Finish	
					2024
					Apr 76
					May 77
					Jun 78
					Jul 79
					Aug 80
CON52210	Install steel roof P2 to LT1	48	30-May-2024	26-Jul-2024	
CON52630	Install steel roof (steel frame) LT1 to P3	18	03-Jun-2024	24-Jun-2024	
CON52430	Construct deck slab, planter wall and roofing PC2 to PC1 (P2 to P1)	30	03-Jun-2024	09-Jul-2024	
CON52650	ABWF works @ steel frame footbridge A1 to P8	48	13-Jun-2024	08-Aug-2024	
CON52830	ABWF works @ escalator pit P3 to LT1	36	25-Jun-2024	06-Aug-2024	
Actual Work Remaining Work Milestone NE/2017/03 Development of Anderson Road Quarry Site - Investigation Design & ConstructionDevelopment of Anderson Road Quarry Site Road - Improvement Works & Pedestrian Connectivity Facilities Works Phase 2A 3-Month Rolling Programme Page 3 of 3					
